


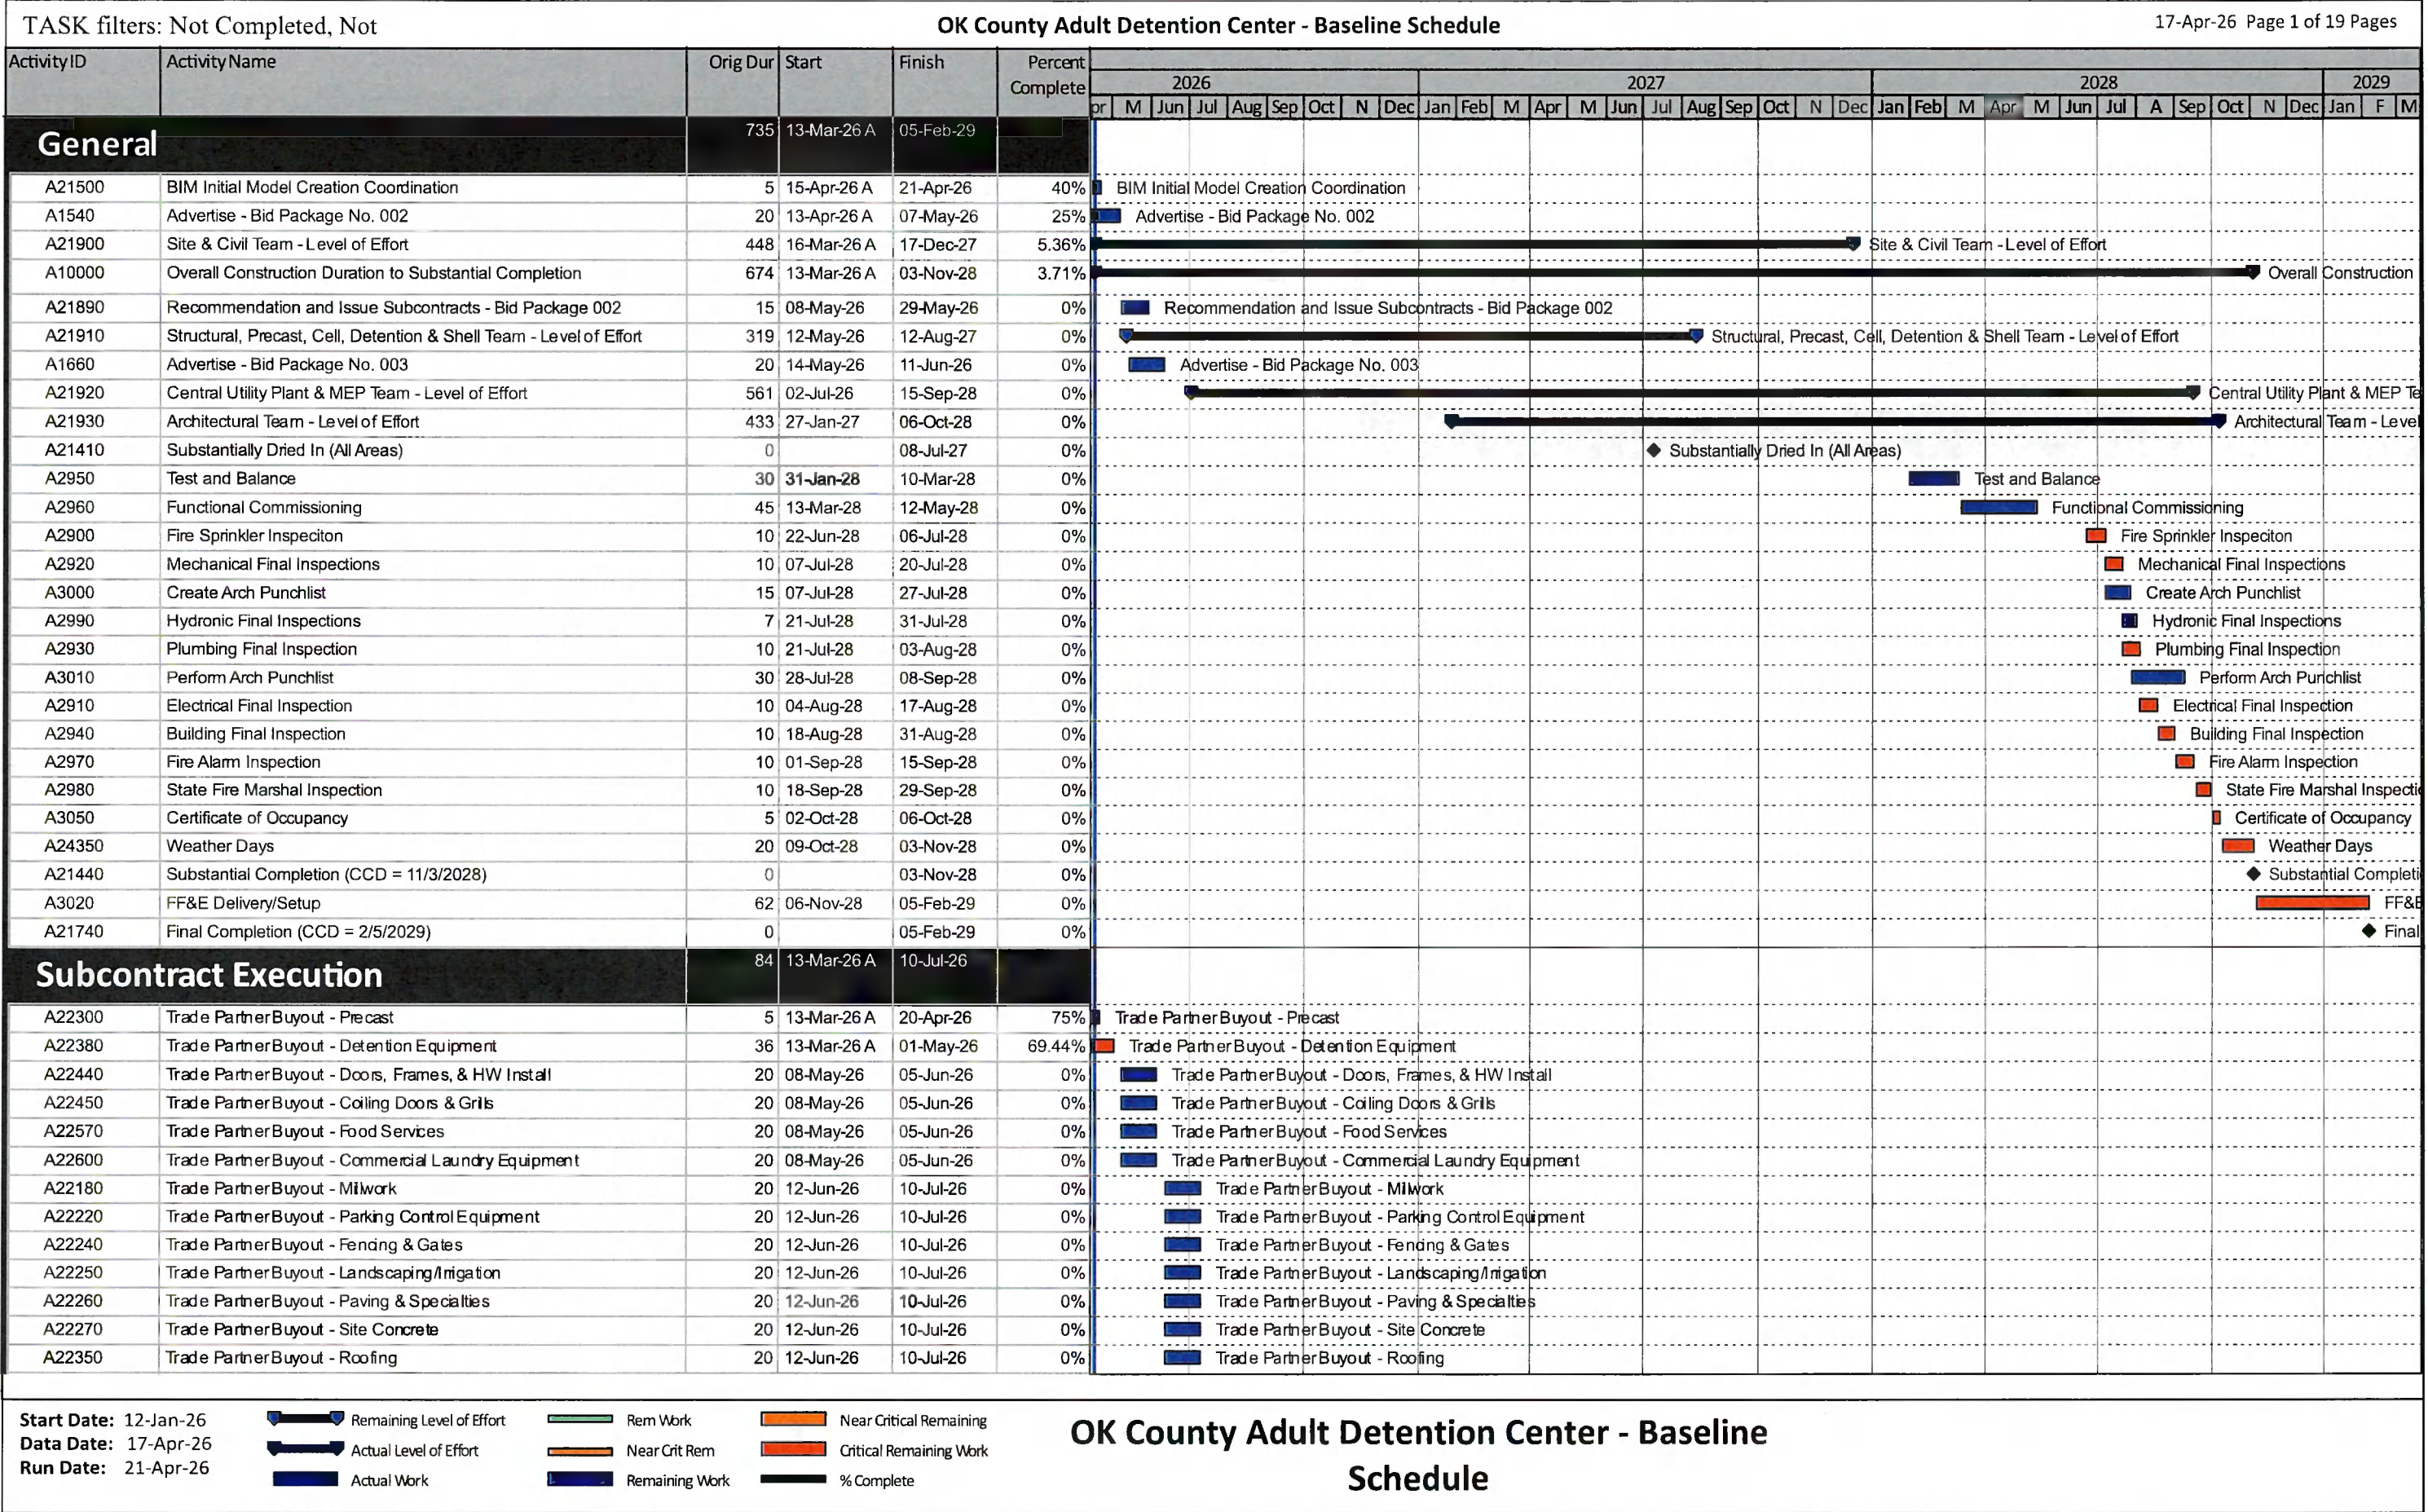

ActivityID	ActivityName	Orig Dur	Start	Finish	Percent Complete																																							
						2026												2027												2028												2029		
						Jan	Feb	M	Apr	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	A	Sep	Oct	N	Dec	Jan	F	M
A22360	Trade Partner Buyout - Fireproofing	20	12-Jun-26	10-Jul-26	0%		Trade Partner Buyout - Fireproofing																																					
A22370	Trade Partner Buyout - EIFS/Stucco	20	12-Jun-26	10-Jul-26	0%		Trade Partner Buyout - EIFS/Stucco																																					
A22470	Trade Partner Buyout - Glass & Glazing	20	12-Jun-26	10-Jul-26	0%		Trade Partner Buyout - Glass & Glazing																																					
A22480	Trade Partner Buyout - Drywall/Acousticals	20	12-Jun-26	10-Jul-26	0%		Trade Partner Buyout - Drywall/Acousticals																																					
A22490	Trade Partner Buyout - Carpet Resilient Tile Flooring	20	12-Jun-26	10-Jul-26	0%		Trade Partner Buyout - Carpet Resilient Tile Flooring																																					
A22510	Trade Partner Buyout - Epoxy Flooring	20	12-Jun-26	10-Jul-26	0%		Trade Partner Buyout - Epoxy Flooring																																					
A22530	Trade Partner Buyout - Paint Wall Covering Coatings	20	12-Jun-26	10-Jul-26	0%		Trade Partner Buyout - Paint Wall Covering Coatings																																					
A22550	Trade Partner Buyout - Signage	20	12-Jun-26	10-Jul-26	0%		Trade Partner Buyout - Signage																																					
A22580	Trade Partner Buyout - Residential Appliances	20	12-Jun-26	10-Jul-26	0%		Trade Partner Buyout - Residential Appliances																																					
A22640	Trade Partner Buyout - Furniture & Accessories	20	12-Jun-26	10-Jul-26	0%		Trade Partner Buyout - Furniture & Accessories																																					
Procurement		288	13-Mar-26 A	29-Apr-27																																								
A23140	Review & Approve - Low Voltage Switchgears	10	06-Apr-26 A	17-Apr-26	90%	Review & Approve - Low Voltage Switchgears																																						
A23480	Review & Approve - Domestic Water Piping	10	06-Apr-26 A	17-Apr-26	90%	Review & Approve - Domestic Water Piping																																						
A23520	Review & Approve - Sanitary Waste & Vent Piping	10	06-Apr-26 A	17-Apr-26	90%	Review & Approve - Sanitary Waste & Vent Piping																																						
A23910	Review & Approve - Panelboards	10	06-Apr-26 A	17-Apr-26	90%	Review & Approve - Panelboards																																						
A24150	Prep & Submit - Structural Steel Submittals - Area T	16	27-Mar-26 A	17-Apr-26	93.75%	Prep & Submit - Structural Steel Submittals - Area T																																						
A23580	Fabricate & Deliver - Sanitary Water Piping	11	06-Apr-26 A	20-Apr-26	81.82%	Fabricate & Deliver - Sanitary Water Piping																																						
A22500	Prep & Submit - Dewatering	20	24-Mar-26 A	20-Apr-26	90%	Prep & Submit - Dewatering																																						
A21290	Review & Approve - Generator Submittal	10	06-Apr-26 A	21-Apr-26	70%	Review & Approve - Generator Submittal																																						
A23340	Review & Approve - Transformers	10	08-Apr-26 A	21-Apr-26	70%	Review & Approve - Transformers																																						
A24300	Prep & Submit - Masonry	22	24-Mar-26 A	22-Apr-26	81.82%	Prep & Submit - Masonry																																						
A23110	Review & Approve - Switchboards	10	10-Apr-26 A	23-Apr-26	50%	Review & Approve - Switchboards																																						
A24200	Prep & Submit - Reinforcing Slab on Metal Deck - Area G	5	17-Apr-26	23-Apr-26	0%	Prep & Submit - Reinforcing Slab on Metal Deck - Area G																																						
A23880	Prep & Submit - Fire Suppression Piping & Sprinklers	29	17-Mar-26 A	24-Apr-26	79.31%	Prep & Submit - Fire Suppression Piping & Sprinklers																																						
A23970	Prep & Submit - Security Electronics	20	30-Mar-26 A	24-Apr-26	70%	Prep & Submit - Security Electronics																																						
A24420	Prep & Submit - Gradebeams, Walls and SOG - Basement T	10	13-Apr-26 A	24-Apr-26	40%	Prep & Submit - Gradebeams, Walls and SOG - Basement T																																						
A24430	Prep & Submit - Gradebeams, Walls and SOG - Crawl Space S	10	13-Apr-26 A	24-Apr-26	40%	Prep & Submit - Gradebeams, Walls and SOG - Crawl Space S																																						
A24440	Prep & Submit - Reinforcing Slab on Metal Deck - Crawl Space S	10	13-Apr-26 A	24-Apr-26	40%	Prep & Submit - Reinforcing Slab on Metal Deck - Crawl Space S																																						
A24770	Review & Approve - Reinforcing Piers - Basement T	10	13-Apr-26 A	24-Apr-26	40%	Review & Approve - Reinforcing Piers - Basement T																																						
A24780	Review & Approve - Reinforcing Piers - Crawl Space S	10	13-Apr-26 A	24-Apr-26	40%	Review & Approve - Reinforcing Piers - Crawl Space S																																						
A21170	Review & Approve - Underslab Plumbing Submittal	10	14-Apr-26 A	27-Apr-26	30%	Review & Approve - Underslab Plumbing Submittal																																						
A23010	Prep & Submit - Exterior Lighting	24	30-Mar-26 A	30-Apr-26	58.33%	Prep & Submit - Exterior Lighting																																						
A23020	Prep & Submit - Emergency Lighting & Exit Signs	24	30-Mar-26 A	30-Apr-26	58.33%	Prep & Submit - Emergency Lighting & Exit Signs																																						
A23380	Prep & Submit - Sanitary Waste Interceptors	35	13-Mar-26 A	30-Apr-26	71.43%	Prep & Submit - Sanitary Waste Interceptors																																						
A23390	Prep & Submit - Sanitary Drains	35	13-Mar-26 A	30-Apr-26	71.43%	Prep & Submit - Sanitary Drains																																						
A24000	Review & Approve - Waterproofing & Sealants	10	17-Apr-26	30-Apr-26	0%	Review & Approve - Waterproofing & Sealants																																						
A24450	Prep & Submit - Gradebeams and SOG - Area T	10	17-Apr-26	30-Apr-26	0%	Prep & Submit - Gradebeams and SOG - Area T																																						
A24460	Prep & Submit - Gradebeams and SOG - Area U/V/W	10	17-Apr-26	30-Apr-26	0%	Prep & Submit - Gradebeams and SOG - Area U/V/W																																						
A24790	Review & Approve - Reinforcing Piers - Area T	10	17-Apr-26	30-Apr-26	0%	Review & Approve - Reinforcing Piers - Area T																																						
A24800	Review & Approve - Reinforcing Piers - Area U/V/W	10	17-Apr-26	30-Apr-26	0%	Review & Approve - Reinforcing Piers - Area U/V/W																																						
A24810	Review & Approve - Reinforcing Piers - Area S	10	17-Apr-26	30-Apr-26	0%	Review & Approve - Reinforcing Piers - Area S																																						
A24820	Review & Approve - Reinforcing Piers - Area L	10	17-Apr-26	30-Apr-26	0%	Review & Approve - Reinforcing Piers - Area L																																						
A24830	Review & Approve - Reinforcing Piers - Area G	10	17-Apr-26	30-Apr-26	0%	Review & Approve - Reinforcing Piers - Area G																																						
A24160	Prep & Submit - Structural Steel Submittals - Area U/V/W & Crawl Space	26	27-Mar-26 A	01-May-26	57.69%	Prep & Submit - Structural Steel Submittals - Area U/V/W & Crawl Space																																						

Start Date: 12-Jan-26

Data Date: 17-Apr-26

Run Date: 21-Apr-26

 Remaining Level of Effort

Actual Level of Effort

Actual Level

 Rem Work

 Near Crit Barn

 Near Cht Rem

 Near Critical Remaining

 Critical Remaining Work

Critical Rem

OK County Adult Detention Center - Baseline Schedule

ActivityID	Activity Name	Orig Dur	Start	Finish	Percent Complete																																						
						2026												2027												2028												2029	
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
A21450	Prep & Submit - Hydronic Pump Submittals	28	26-Mar-26	A	04-May-26	57.14%		Prep & Submit - Hydronic Pump Submittals																																			
A22760	Prep & Submit - Expansion Tanks & Air Separators	28	26-Mar-26	A	04-May-26	57.14%		Prep & Submit - Expansion Tanks & Air Separators																																			
A22810	Prep & Submit - Water Heaters & Storage Tanks	28	26-Mar-26	A	04-May-26	57.14%		Prep & Submit - Water Heaters & Storage Tanks																																			
A22830	Prep & Submit - Filtration Systems	28	26-Mar-26	A	04-May-26	57.14%		Prep & Submit - Filtration Systems																																			
A22850	Prep & Submit - Water Softener Package	28	26-Mar-26	A	04-May-26	57.14%		Prep & Submit - Water Softener Package																																			
A22880	Prep & Submit - Domestic Booster Pump	28	26-Mar-26	A	04-May-26	57.14%		Prep & Submit - Domestic Booster Pump																																			
A22940	Prep & Submit - Heat Recovery & Air Cooled Chillers	28	26-Mar-26	A	04-May-26	57.14%		Prep & Submit - Heat Recovery & Air Cooled Chillers																																			
A22980	Prep & Submit - Hot Water Coils	28	26-Mar-26	A	04-May-26	57.14%		Prep & Submit - Hot Water Coils																																			
A23420	Prep & Submit - Plumbing Fixtures	28	26-Mar-26	A	04-May-26	57.14%		Prep & Submit - Plumbing Fixtures																																			
A24140	Fabricate & Deliver - Domestic Water Vault	15	15-Apr-26	A	05-May-26	13.33%		Fabricate & Deliver - Domestic Water Vault																																			
A21340	Prep & Submit - VAV Submittals	30	26-Mar-26	A	06-May-26	53.33%		Prep & Submit - VAV Submittals																																			
A21370	Prep & Submit - FCUs Submittals	30	26-Mar-26	A	06-May-26	53.33%		Prep & Submit - FCUs Submittals																																			
A23080	Prep & Submit - Pre-Fab Cells	15	17-Apr-26		07-May-26	0%		Prep & Submit - Pre-Fab Cells																																			
A21070	Prep & Submit - Reinforcing Slab on Metal Deck - Basement T	19	13-Apr-26	A	07-May-26	21.05%		Prep & Submit - Reinforcing Slab on Metal Deck - Basement T																																			
A24170	Prep & Submit - Structural Steel Submittals - Area S	31	27-Mar-26	A	08-May-26	48.39%		Prep & Submit - Structural Steel Submittals - Area S																																			
A24470	Prep & Submit - Gradebeams and SOG -Area S	18	17-Apr-26		12-May-26	0%		Prep & Submit - Gradebeams and SOG -Area S																																			
A24480	Prep & Submit - Gradebeams and SOG -Area L	18	17-Apr-26		12-May-26	0%		Prep & Submit - Gradebeams and SOG -Area L																																			
A24490	Prep & Submit - Gradebeams and SOG -Area G	18	17-Apr-26		12-May-26	0%		Prep & Submit - Gradebeams and SOG -Area G																																			
A24180	Prep & Submit - Structural Steel Submittals -Area L	36	27-Mar-26	A	15-May-26	41.67%		Prep & Submit - Structural Steel Submittals -Area L																																			
A24190	Prep & Submit - Structural Steel Submittals -Area G	36	27-Mar-26	A	15-May-26	41.67%		Prep & Submit - Structural Steel Submittals -Area G																																			
A21220	Prep & Submit - Cooling Tower Submittals	45	26-Mar-26	A	28-May-26	35.56%		Prep & Submit - Cooling Tower Submittals																																			
A21190	Prep & Submit - Boiler Submittals	60	26-Mar-26	A	18-Jun-26	26.67%		Prep & Submit - Boiler Submittals																																			
A21250	Prep & Submit - Electrical Gear Submittals	60	30-Mar-26	A	22-Jun-26	23.33%		Prep & Submit - Electrical Gear Submittals																																			
A21310	Prep & Submit - AHU Submittals	90	26-Mar-26	A	31-Jul-26	17.78%		Prep & Submit - AHU Submittals																																			
A24210	Review & Approve - Structural Steel Submittals - Area T	10	20-Apr-26		01-May-26	0%		Review & Approve - Structural Steel Submittals - Area T																																			
A23540	Fabricate & Deliver - Domestic Water Piping	15	20-Apr-26		08-May-26	0%		Fabricate & Deliver - Domestic Water Piping																																			
A23810	Fabrication & Delivery - Panelboards	120	20-Apr-26		07-Oct-26	0%		Fabrication & Delivery - Panelboards																																			
A23220	Fabrication & Delivery - Low Voltage Switchgears	260	20-Apr-26		27-Apr-27	0%		Fabrication & Delivery - Low Voltage Switchgears																																			
A1160	Prep & Submit - Precast Wall Coordination	25	20-Mar-26	A	27-Apr-26	80%		Prep & Submit - Precast Wall Coordination																																			
A24410	Fabricate & Deliver - Dewatering	5	21-Apr-26		27-Apr-26	0%		Fabricate & Deliver - Dewatering																																			
A24400	Review & Approve - Dewatering	10	21-Apr-26		04-May-26	0%		Review & Approve - Dewatering																																			
A23350	Fabrication & Delivery - Transformers	150	22-Apr-26		20-Nov-26	0%		Fabrication & Delivery - Transformers																																			
A21300	Fabrication & Delivery - Generator	260	22-Apr-26		29-Apr-27	0%		Fabrication & Delivery - Generator																																			
A24310	Review & Approve - Masonry	10	23-Apr-26		06-May-26	0%		Review & Approve - Masonry																																			
A24590	Review & Approve - Reinforcing Slab on Metal Deck - Area G	10	24-Apr-26		07-May-26	0%		Review & Approve - Reinforcing Slab on Metal Deck - Area G																																			
A23190	Fabrication & Delivery - Switchboards	160	24-Apr-26		10-Dec-26	0%		Fabrication & Delivery - Switchboards																																			
A23890	Review & Approve - Fire Suppression Piping & Sprinklers	10	27-Apr-26		08-May-26	0%		Review & Approve - Fire Suppression Piping & Sprinklers																																			
A23980	Review & Approve - Security Electronics	10	27-Apr-26		08-May-26	0%		Review & Approve - Security Electronics																																			
A24500	Review & Approve - Gradebeams, Walls and SOG - Basement T	10	27-Apr-26		08-May-26	0%		Review & Approve - Gradebeams, Walls and SOG - Basement T																																			
A24520	Review & Approve - Gradebeams, Walls and SOG - Crawl Space S	10	27-Apr-26		08-May-26	0%		Review & Approve - Gradebeams, Walls and SOG - Crawl Space S																																			
A24530	Review & Approve - Reinforcing Slab on Metal Deck - Crawl Space S	10	27-Apr-26		08-May-26	0%		Review & Approve - Reinforcing Slab on Metal Deck - Crawl Space S																																			
A24840	Fab & Deliver - Reinforcing Piers - Basement T	10	27-Apr-26		08-May-26	0%		Fab & Deliver - Reinforcing Piers - Basement T																																			
A24850	Fab & Deliver - Reinforcing Piers - Crawl Space S	10	27-Apr-26		08-May-26	0%		Fab & Deliver - Reinforcing Piers - Crawl Space S																																			
A1170	Review & Approve - Precast Wall Shop Drawings	10	27-Apr-26		11-May-26	0%		Review & Approve - Precast Wall Shop Drawings																																			
A21180	Fabrication & Delivery - Underslab Plumbing	20	28-Apr-26		26-May-26	0%		Fabrication & Delivery - Underslab Plumbing																																			

Start Date: 12-Jan-26

Data Date: 17-Apr-26

Run Date: 21-Apr-26

 Remaining Level of Effort

Actual Level of Effort

 Actual Work

 Rem Work

 Near Crit Rem

 Near Cut Rest
 Remaining Work

 Near Critical Remaining

Critical Remaining Work

■ Critical Review

■ % Complete

OK County Adult Detention Center - Baseline Schedule

ActivityID	ActivityName	Orig Dur	Start	Finish	Percent Complete	2026																															2027												2028												2029		
						2026												2027												2028												2029																					
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar																			
A23090	Review & Approve - Exterior Lighting	10	01-May-26	14-May-26	0%																																																										
A23100	Review & Approve - Emergency Lighting & Exit Signs	10	01-May-26	14-May-26	0%																																																										
A23490	Review & Approve - Sanitary Waste Interceptors	10	01-May-26	14-May-26	0%																																																										
A23500	Review & Approve - Sanitary Drains	10	01-May-26	14-May-26	0%																																																										
A24540	Review & Approve - Gradebeams and SOG - Area T	10	01-May-26	14-May-26	0%																																																										
A24550	Review & Approve - Gradebeams and SOG - Area U/V/W	10	01-May-26	14-May-26	0%																																																										
A24860	Fab & Deliver - Reinforcing Piers - Area T	10	01-May-26	14-May-26	0%																																																										
A24870	Fab & Deliver - Reinforcing Piers - Area U/V/W	10	01-May-26	14-May-26	0%																																																										
A24880	Fab & Deliver - Reinforcing Piers - Area S	10	01-May-26	14-May-26	0%																																																										
A24890	Fab & Deliver - Reinforcing Piers - Area L	10	01-May-26	14-May-26	0%																																																										
A24900	Fab & Deliver - Reinforcing Piers - Area G	10	01-May-26	14-May-26	0%																																																										
A23550	Fabricate & Deliver - Sanitary Waste Interceptors	11	01-May-26	15-May-26	0%																																																										
A23560	Fabricate & Deliver - Sanitary Drains	11	01-May-26	15-May-26	0%																																																										
A24010	Fabrication & Delivery - Waterproofing & Sealants	45	01-May-26	06-Jul-26	0%																																																										
A24220	Review & Approve - Structural Steel Submittals - Area U/V/W	10	04-May-26	15-May-26	0%																																																										
A21010	Prep & Submit - Detention Hollow Metal Frame Submittals	30	04-May-26	15-Jun-26	0%																																																										
A21090	Fabrication & Delivery - Structural Steel - Area T	30	04-May-26	15-Jun-26	0%																																																										
A21460	Review & Approve - Hydronic Pumps	10	05-May-26	18-May-26	0%																																																										
A22770	Review & Approve - Expansion Tanks & Air Separators	10	05-May-26	18-May-26	0%																																																										
A22800	Review & Approve - Water Heaters & Storage Tanks	10	05-May-26	18-May-26	0%																																																										
A22820	Review & Approve - Filtration Systems	10	05-May-26	18-May-26	0%																																																										
A22860	Review & Approve - Water Softener Package	10	05-May-26	18-May-26	0%																																																										
A22890	Review & Approve - Domestic Booster Pump	10	05-May-26	18-May-26	0%																																																										
A22950	Review & Approve - Heat Recovery & Air Cooled Chillers	10	05-May-26	18-May-26	0%																																																										
A22970	Review & Approve - Hot Water Coils	10	05-May-26	18-May-26	0%																																																										
A23600	Review & Approve - Plumbing Fixtures	10	05-May-26	18-May-26	0%																																																										
A21350	Review & Approve - VAV Submittal	10	07-May-26	20-May-26	0%																																																										
A21380	Review & Approve - FCUs Submittal	10	07-May-26	20-May-26	0%																																																										
A24320	Fabrication & Delivery - Masonry	40	07-May-26	02-Jul-26	0%																																																										
A24690	Fab & Deliver - Reinforcing Slab on Metal Deck - Area G	5	08-May-26	14-May-26	0%																																																										
A23160	Review & Approve - Pre-Fab Cells	10	08-May-26	21-May-26	0%																																																										
A24510	Review & Approve - Reinforcing Slab on Metal Deck - Basement T	10	08-May-26	21-May-26	0%																																																										
A24630	Fab & Deliver - Reinforcing Slab on Metal Deck - Crawl Space S	5	11-May-26	15-May-26	0%																																																										
A24230	Review & Approve - Structural Steel Submittals - Area S	10	11-May-26	22-May-26	0%																																																										
A24600	Fab & Deliver - Gradebeams, Walls and SOG - Basement T	10	11-May-26	22-May-26	0%																																																										
A24620	Fab & Deliver - Gradebeams, Walls and SOG - Crawl Space S	10	11-May-26	22-May-26	0%																																																										
A23900	Fabrication & Delivery - Fire Suppression Piping & Sprinklers	70	11-May-26	18-Aug-26	0%																																																										
A23990	Fabrication & Delivery - Security Electronics	85	11-May-26	09-Sep-26	0%																																																										
A24560	Review & Approve - Gradebeams and SOG - Area S	10	13-May-26	27-May-26	0%																																																										
A24570	Review & Approve - Gradebeams and SOG - Area L	10	13-May-26	27-May-26	0%																																																										
A24580	Review & Approve - Gradebeams and SOG - Area G	10	13-May-26	27-May-26	0%																																																										
A24640	Fab & Deliver - Gradebeams and SOG - Area T	10	15-May-26	29-May-26	0%																																																										
A24650	Fab & Deliver - Gradebeams and SOG - Area U/V/W	10	15-May-26	29-May-26	0%																																																										
A23170	Fabrication & Delivery - Exterior Lighting	80	15-May-26	08-Sep-26	0%																																																										
A23180	Fabrication & Delivery - Emergency Lighting & Exit Signs	80	15-May-26	08-Sep-26	0%																																																										

Start Date: 12-Jan-26

Data Date: 17-Apr-26

Run Date: 21-Apr-26

 Remaining Level of Effort

Actual Level of Effort

 Actual Work

Rem Work

 Near Crit Rem

 Near-Crit Rem

 Remaining Work

 Near Critical Remaining

 Critical Remaining Work

Critical Remarks

% Complete

OK County Adult Detention Center - Baseline Schedule

ActivityID	Activity Name	Orig Dur	Start	Finish	Percent Complete	2026																																				2027												2028												2029		
						2026												2027												2028												2029																										
						pr	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	A	Sep	Oct	N	Dec	Jan	F	M																											
A24240	Review & Approve - Structural Steel Submittals - Area L	10	18-May-26	01-Jun-26	0%		Review & Approve - Structural Steel Submittals - Area L																																																													
A24250	Review & Approve - Structural Steel Submittals - Area G	10	18-May-26	01-Jun-26	0%		Review & Approve - Structural Steel Submittals - Area G																																																													
A21110	Fabrication & Delivery - Structural Steel -Area U/V/W	30	18-May-26	29-Jun-26	0%		Fabrication & Delivery - Structural Steel -Area U/V/W																																																													
A22990	Fabrication & Delivery - Hot Water Coils	20	19-May-26	16-Jun-26	0%		Fabrication & Delivery - Hot Water Coils																																																													
A23610	Fabrication & Delivery - Plumbing Fixtures	50	19-May-26	29-Jul-26	0%		Fabrication & Delivery - Plumbing Fixtures																																																													
A22790	Fabrication & Delivery - Water Heaters & Storage Tanks	60	19-May-26	12-Aug-26	0%		Fabrication & Delivery - Water Heaters & Storage Tanks																																																													
A22840	Fabrication & Delivery - Filtration Systems	70	19-May-26	26-Aug-26	0%		Fabrication & Delivery - Filtration Systems																																																													
A22900	Fabrication & Delivery - Domestic Booster Pump	80	19-May-26	10-Sep-26	0%		Fabrication & Delivery - Domestic Booster Pump																																																													
A22960	Fabrication & Delivery - Heat Recovery & Air Cooled Chillers	90	19-May-26	24-Sep-26	0%		Fabrication & Delivery - Heat Recovery & Air Cooled Chillers																																																													
A21470	Fabrication & Delivery - Hydronic Pumps	100	19-May-26	08-Oct-26	0%		Fabrication & Delivery - Hydronic Pumps																																																													
A22870	Fabrication & Delivery - Water Softener Package	130	19-May-26	19-Nov-26	0%		Fabrication & Delivery - Water Softener Package																																																													
A22780	Fabrication & Delivery - Expansion Tanks & Air Separators	200	19-May-26	03-Mar-27	0%		Fabrication & Delivery - Expansion Tanks & Air Separators																																																													
A21360	Fabrication & Delivery - VAV - Area	60	21-May-26	14-Aug-26	0%		Fabrication & Delivery - VAV - Area																																																													
A21390	Fabrication & Delivery - FCUs	60	21-May-26	14-Aug-26	0%		Fabrication & Delivery - FCUs																																																													
A24610	Fab & Deliver - Reinforcing Slab on Metal Deck - Basement T	5	22-May-26	29-May-26	0%		Fab & Deliver - Reinforcing Slab on Metal Deck - Basement T																																																													
A23620	Fabrication & Delivery - Pre-Fab Cells	166	22-May-26	19-Jan-27	0%		Fabrication & Delivery - Pre-Fab Cells																																																													
A21130	Fabrication & Delivery - Structural Steel - Area S	30	26-May-26	07-Jul-26	0%		Fabrication & Delivery - Structural Steel - Area S																																																													
A24660	Fab & Deliver - Gradebeams and SOG - Area S	10	28-May-26	10-Jun-26	0%		Fab & Deliver - Gradebeams and SOG - Area S																																																													
A24670	Fab & Deliver - Gradebeams and SOG - Area L	10	28-May-26	10-Jun-26	0%		Fab & Deliver - Gradebeams and SOG - Area L																																																													
A24680	Fab & Deliver - Gradebeams and SOG - Area G	10	28-May-26	10-Jun-26	0%		Fab & Deliver - Gradebeams and SOG - Area G																																																													
A21230	Review & Approve - Cooling Tower Submittal	10	29-May-26	11-Jun-26	0%		Review & Approve - Cooling Tower Submittal																																																													
A21140	Fabrication & Delivery - Structural Steel - Area L	30	02-Jun-26	14-Jul-26	0%		Fabrication & Delivery - Structural Steel - Area L																																																													
A21150	Fabrication & Delivery - Structural Steel - Area G	30	02-Jun-26	14-Jul-26	0%		Fabrication & Delivery - Structural Steel - Area G																																																													
A23040	Prep & Submit - Laundry Equipment	15	08-Jun-26	26-Jun-26	0%		Prep & Submit - Laundry Equipment																																																													
A23050	Prep & Submit - Overhead Coiling Doors	15	08-Jun-26	26-Jun-26	0%		Prep & Submit - Overhead Coiling Doors																																																													
A23930	Prep & Submit - Food Services Equipment	15	08-Jun-26	26-Jun-26	0%		Prep & Submit - Food Services Equipment																																																													
A21040	Prep & Submit - Hollow Metal Door Frames Submittals	30	08-Jun-26	20-Jul-26	0%		Prep & Submit - Hollow Metal Door Frames Submittals																																																													
A24280	Prep & Submit - Cooling Tower Shop Drawings	10	12-Jun-26	25-Jun-26	0%		Prep & Submit - Cooling Tower Shop Drawings																																																													
A21240	Fabrication & Delivery - Cooling Towers	90	12-Jun-26	19-Oct-26	0%		Fabrication & Delivery - Cooling Towers																																																													
A21020	Review & Approve - Detention Hollow Metal Frame Submittal	10	16-Jun-26	29-Jun-26	0%		Review & Approve - Detention Hollow Metal Frame Submittal																																																													
A21200	Review & Approve - Boiler Submittal	10	19-Jun-26	02-Jul-26	0%		Review & Approve - Boiler Submittal																																																													
A21260	Review & Approve - Electrical Gear Submittal	10	23-Jun-26	07-Jul-26	0%		Review & Approve - Electrical Gear Submittal																																																													
A21580	Fabrication & Delivery - Structural Steel - MEP Trestle	25	25-Jun-26	30-Jul-26	0%		Fabrication & Delivery - Structural Steel - MEP Trestle																																																													
A24290	Review & Approve - Cooling Tower Shop Drawings	10	26-Jun-26	10-Jul-26	0%		Review & Approve - Cooling Tower Shop Drawings																																																													
A23120	Review & Approve - Laundry Equipment	10	29-Jun-26	13-Jul-26	0%		Review & Approve - Laundry Equipment																																																													
A23130	Review & Approve - Overhead Coiling Doors	10	29-Jun-26	13-Jul-26	0%		Review & Approve - Overhead Coiling Doors																																																													
A23260	Review & Approve - Food Services Equipment	10	29-Jun-26	13-Jul-26	0%		Review & Approve - Food Services Equipment																																																													
A1360	Fabrication & Delivery - Precast Walls	80	30-Jun-26	21-Oct-26	0%		Fabrication & Delivery - Precast Walls																																																													
A21030	Fabrication & Delivery - Detention Hollow Metal Frame	80	30-Jun-26	21-Oct-26	0%		Fabrication & Delivery - Detention Hollow Metal Frame																																																													
A21210	Fabrication & Delivery - Boiler	65	06-Jul-26	05-Oct-26	0%		Fabrication & Delivery - Boiler																																																													
A21270	Fabrication & Delivery - Electrical Gear	180	08-Jul-26	23-Mar-27	0%		Fabrication & Delivery - Electrical Gear																																																													
A22420	Prep & Submit - Site Concrete	10	13-Jul-26	24-Jul-26	0%		Prep & Submit - Site Concrete																																																													
A23250	Prep & Submit - Residential Appliances	15	13-Jul-26	31-Jul-26	0%		Prep & Submit - Residential Appliances																																																													
A23440	Prep & Submit - Roofing	15	13-Jul-26	31-Jul-26	0%		Prep & Submit - Roofing																																																													
A23660	Prep & Submit - Drywall	15	13-Jul-26	31-Jul-26	0%		Prep & Submit - Drywall																																																													

Start Date: 12-Jan-26

Data Date: 17-Apr-26

Run Date: 21-Apr-26

Remaining Level of Effort

Actual Level of Effort

Actual Level 1

 Rem Work

 Near Crit Rem

 Near Cnt Rem

 Near Critical Remaining

 Critical Remaining Work

Critical Rem

OK County Adult Detention Center - Baseline Schedule

TASK filters: Not Completed, Not

OK County Adult Detention Center - Baseline Schedule

ActivityID	ActivityName	Orig Dur	Start	Finish	Percent Complete	2026												2027												2028												2029																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																

Start Date: 12-Jan-26
Data Date: 17-Apr-26
Run Date: 21-Apr-26



Remaining Level of Effort
Actual Level of Effort
Actual Work



Rem Work
Near Crit Rem
Remaining Work



Near Critical Remaining
Critical Remaining Work
% Complete

OK County Adult Detention Center - Baseline
Schedule

TASK filters: Not Completed, Not

OK County Adult Detention Center - Baseline Schedule

17-Apr-26 Page 7 of 19 Pages

ActivityID	ActivityName	Orig Dur	Start	Finish	Percent Complete	2026												2027												2028												2029		
						or	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	A	Sep	Oct	N	Dec	Jan	F	M			
A24070	Fabrication & Delivery - Fireproofing	75	17-Aug-26	02-Dec-26	0%																																							
A24100	Fabrication & Delivery - Resilient Tile Flooring	75	17-Aug-26	02-Dec-26	0%																																							
A24110	Fabrication & Delivery - Epoxy Flooring	75	17-Aug-26	02-Dec-26	0%																																							
A23290	Fabrication & Delivery - Residential Appliances	80	17-Aug-26	09-Dec-26	0%																																							
A23680	Fabrication & Delivery - Drywall	80	17-Aug-26	09-Dec-26	0%																																							
A23460	Fabrication & Delivery - Roofing	85	17-Aug-26	16-Dec-26	0%																																							
A23960	Fabrication & Delivery - Glass & Glazing	85	17-Aug-26	16-Dec-26	0%																																							
A23700	Fabrication & Delivery - Parking Control Equipment	90	17-Aug-26	23-Dec-26	0%																																							
A23730	Fabrication & Delivery - Furniture & Accessories	105	17-Aug-26	15-Jan-27	0%																																							
A23850	Fabrication & Delivery - Signage	75	24-Aug-26	09-Dec-26	0%																																							
A23650	Fabrication & Delivery - Millwork	80	31-Aug-26	23-Dec-26	0%																																							
Sitework		453	09-Mar-26 A	17-Dec-27																																								
A19940	Install Sanitary Sewer	40	07-Apr-26 A	02-Jun-26	20%																																							
A1950	OG&E - Power Design/Procurement	180	09-Mar-26 A	18-Nov-26	16.11%																																							
A19610	Install Domestic Water Vault	20	06-May-26	03-Jun-26	0%																																							
A1530	Sanitary Line Re Route	7	15-Apr-26 A	21-May-26	50%																																							
A19620	Excavate Domestic Water Lines	30	21-May-26	06-Jul-26	0%																																							
A19690	Install Storm - East	30	03-Jun-26	15-Jul-26	0%																																							
A19630	Install Domestic Water & Fire Lines to Area T	10	06-Jul-26	20-Jul-26	0%																																							
A19650	Install Underground Electrical Duct Bank	26	06-Jul-26	11-Aug-26	0%																																							
A19730	Excavate Domestic Water Line & Sanitary Sewer Line	10	20-Jul-26	03-Aug-26	0%																																							
A19770	Excavate for Duct Bank	10	03-Aug-26	17-Aug-26	0%																																							
A19750	Install Domestic Water and Sanitary Line	15	03-Aug-26	24-Aug-26	0%																																							
A23000	Building Pad Complete	0		13-Aug-26	0%																																							
A19780	Install Underground Duct Bank to Transformers	10	17-Aug-26	31-Aug-26	0%																																							
A19700	Install Storm - West	20	24-Aug-26	21-Sep-26	0%																																							
A20070	Install Grease Interceptor	8	31-Aug-26	10-Sep-26	0%																																							
A1820	Install OG&E North Duct Bank	15	19-Nov-26	11-Dec-26	0%																																							
A1850	Pull OG&E Feeder Cables - North Side	10	14-Dec-26	28-Dec-26	0%																																							
A1840	Install OG&E South Duct Bank	15	14-Dec-26	05-Jan-27	0%																																							
A22690	Set OG&E Transformers - North Side	5	29-Dec-26	05-Jan-27	0%																																							
A22680	Pull OG&E Feeder Cables - South Side	10	06-Jan-27	19-Jan-27	0%																																							
A22700	Set OG&E Transformers - South Side	5	20-Jan-27	26-Jan-27	0%																																							
A21400	Structural Completion	0		23-Mar-27	0%																																							
A3140	Rough Grade - West Drive Lane and Landscape Areas	10	30-Jul-27	12-Aug-27	0%																																							
A19480	Rough Grade - Parking Lot and Landscape Areas	8	13-Aug-27	24-Aug-27	0%																																							
A3150	Excavate West Detention Pond	10	13-Aug-27	26-Aug-27	0%																																							
A19500	Fine Grade - South Side	5	25-Aug-27	31-Aug-27	0%																																							
A19590	Rough Grade for Future Site	15	25-Aug-27	15-Sep-27	0%																																							
A3160	Fine Grade - West Drive Lane	8	27-Aug-27	08-Sep-27	0%																																							
A19510	Install Agg Base and Base Coat - South Parking Lot	15	01-Sep-27	22-Sep-27	0%																																							
A3170	Install Agg Base and Base Coat - West Drive Lane	10	09-Sep-27	22-Sep-27	0%																																							
A19600	Erect Fencing for Site Separation	10	16-Sep-27	29-Sep-27	0%																																							

Start Date: 12-Jan-26

Data Date: 17-Apr-26

Run Date: 21-Apr-26



Remaining Level of Effort



Actual Level of Effort



Actual Work



Rem Work



Near Crit Rem



Remaining Work



Near Critical Remaining



Critical Remaining Work



% Complete

OK County Adult Detention Center - Baseline Schedule

TASK filters: Not Completed, Not

OK County Adult Detention Center - Baseline Schedule

17-Apr-26 Page 8 of 19 Pages

ActivityID	ActivityName	Orig Dur	Start	Finish	Percent Complete	2026												2027												2028												2029																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		

Start Date: 12-Jan-26

Data Date: 17-Apr-26

Run Date: 21-Apr-26



Remaining Level of Effort



Actual Level of Effort



Actual Work



Rem Work



Near Crit Rem



Remaining Work



Near Critical Remaining



Critical Remaining Work



% Complete

OK County Adult Detention Center - Baseline
Schedule

TASK filters: Not Completed, Not

OK County Adult Detention Center - Baseline Schedule

17-Apr-26 Page 9 of 19 Pages

ActivityID	ActivityName	Orig Dur	Start	Finish	Percent Complete																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
						2026												2027												2028												2029																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
A19390	Form and Pour Basement Walls - Area S Crawl Space	15	12-Jun-26	06-Jul-26	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		</

Start Date: 12-Jan-26
Data Date: 17-Apr-26
Run Date: 21-Apr-26

 Remaining Level of Effort
 Actual Level of Effort
 Actual Work

 Rem Work
 Near Crit Rem
 Remaining Work

 Near Critical Remaining
 Critical Remaining Work
 % Complete

OK County Adult Detention Center - Baseline
Schedule

TASK filters: Not Completed, Not

OK County Adult Detention Center - Baseline Schedule

17-Apr-26 Page 10 of 19 Pages

ActivityID	ActivityName	Orig Dur	Start	Finish	Percent Complete																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
						2026												2027												2028										2029																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
A17630	Erect MEP Trestle/Structure	30	14-Jan-27	24-Feb-27	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									

Start Date: 12-Jan-26
Data Date: 17-Apr-26
Run Date: 21-Apr-26

 Remaining Level of Effort
 Actual Level of Effort
 Actual Work

 Rem Work
 Near Crit Rem
 Remaining Work

 Near Critical Remaining
 Critical Remaining Work
 % Complete

OK County Adult Detention Center - Baseline
Schedule

[illegible]

Start Date: 12-Jan-26

Data Date: 17-Apr-26

Run Date: 21-Apr-26

 Remaining Level of Effort

Actual Level of Effort

Actual Level C

 Rem Work

 Near Crit Rem

■ Near Crit Renl

 Near Critical Remaining

 Critical Remaining Work

Critical Reflection

OK County Adult Detention Center - Baseline Schedule

TASK filters: Not Completed, Not

OK County Adult Detention Center - Baseline Schedule

17-Apr-26 Page 12 of 19 Pages

ActivityID	ActivityName	Orig Dur	Start	Finish	Percent Complete	2026												2027												2028												2029																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
						pr	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	A	Sen	Oct	N	Dec	Jan	F	M																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
A2080	Form and Pour Platform - Area V/W	6	01-Sep-26	09-Sep-26	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									

Start Date: 12-Jan-26

Data Date: 17-Apr-26

Run Date: 21-Apr-26

Remaining Level of Effort

Actual Level of Effort

Actual Work

Rem Work

Near Crit Rem

Remaining Work

Near Critical Remaining

Critical Remaining Work

% Complete

OK County Adult Detention Center - Baseline Schedule

OK County Adult Detention Center - Baseline Schedule

ActivityID	ActivityName	Orig Dur	Start	Finish	Percent Complete	2026												2027												2028												2029		
						Dr	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	A	Sep	Oct	N	Dec	Jan	F	M			
A1810	Drill Piers - Area S	8	29-May-26	10-Jun-26	0%																																							
A21620	Overhead Coordination - Area S - Crawl Space	35	03-Jun-26	22-Jul-26	0%																																							
A1910	Form and Pour Grade Beams - Area S	10	13-Jul-26	24-Jul-26	0%																																							
A1960	Concrete Curing - Area S	7	27-Jul-26	04-Aug-26	0%																																							
A2010	Install Underground MEP - Area S	25	27-Jul-26	28-Aug-26	0%																																							
A1940	Pour SOG - Area S - P1	12	26-Oct-26	10-Nov-26	0%																																							
A2090	Pour SOG - Area S - P2	12	11-Nov-26	30-Nov-26	0%																																							
A2100	Pour SOG - Area S - P3	12	01-Dec-26	16-Dec-26	0%																																							
A22060	L1 Overhead Coordination - Area S	49	23-Dec-26	03-Mar-27	0%																																							
A16520	Erect Precast Walls - Area S - South Half	10	29-Dec-26	12-Jan-27	0%																																							
A17510	Erect Precast Walls - Area S - North Half	10	10-Feb-27	23-Feb-27	0%																																							
A16560	Erect HSS Columns - Area S	8	24-Feb-27	05-Mar-27	0%																																							
A16570	Install Roof Joists - Area S	12	08-Mar-27	23-Mar-27	0%																																							
A17450	Lay Roof Decking - Area S	12	24-Mar-27	08-Apr-27	0%																																							
A18630	Set Roof Units - Area S	5	09-Apr-27	15-Apr-27	0%																																							
A21710	Install SOG Leave Outs - Area S	10	09-Apr-27	22-Apr-27	0%																																							
A18490	Install Roofing - Area S	12	16-Apr-27	03-May-27	0%																																							
A16580	Remove Precast Bracing - Area S	5	23-Apr-27	29-Apr-27	0%																																							
A17430	Build Priority CMU Walls - Area S	10	30-Apr-27	13-May-27	0%																																							
A16920	OH Plumbing Rough In - Storm - Area S	15	30-Apr-27	20-May-27	0%																																							
A18500	Install Exterior Doors and Louvers - Area S	10	04-May-27	17-May-27	0%																																							
A18590	Install Exterior Windows - Area S	10	04-May-27	17-May-27	0%																																							
A18050	Set OG&E Disconnects	5	14-May-27	20-May-27	0%																																							
A16950	Electrical Room Build Out - Area S	10	14-May-27	27-May-27	0%																																							
A17440	Build CMU Walls - Area S	30	14-May-27	25-Jun-27	0%																																							
A22130	Substantially Dry - Area S	0		17-May-27	0%																																							
A18520	Place Elastomeric Coating - Area S	15	18-May-27	08-Jun-27	0%																																							
A18060	Set Switchgears - Normal Power	5	21-May-27	27-May-27	0%																																							
A18100	Set Exterior Switchboard Disconnects	5	21-May-27	27-May-27	0%																																							
A16960	OH Plumbing Rough In - Domestic - Area S	25	21-May-27	25-Jun-27	0%																																							
A16970	OH Hydronic Rough In - Area S	35	21-May-27	12-Jul-27	0%																																							
A18070	Set Transformers - Normal Power	5	28-May-27	04-Jun-27	0%																																							
A18130	Set Generators	5	28-May-27	04-Jun-27	0%																																							
A18260	Set Switchgears - Standby	5	28-May-27	04-Jun-27	0%																																							
A16990	OH Electrical Rough In - Area S	25	28-May-27	02-Jul-27	0%																																							
A18270	Set ATS	5	07-Jun-27	11-Jun-27	0%																																							
A18280	Set Transformers - UPS	5	07-Jun-27	11-Jun-27	0%																																							

Start Date: 12-Jan-26
Data Date: 17-Apr-26
Run Date: 21-Apr-26

 Remaining Level of Effort
 Actual Level of Effort
 Actual Work
 Rem Work
 Near Crit Rem
 Remaining Work
 Near Critical Remaining
 Critical Remaining Work
 % Complete

OK County Adult Detention Center - Baseline
Schedule

[illegible]

Start Date: 12-Jan-26
Data Date: 17-Apr-26
Run Date: 21-Apr-26

 Remaining Level of Effort
 Actual Level of Effort
 Actual Work

-  Rem Work
-  Near Crit Rem
- Remaining Work

 Near Critical Remaining
 Critical Remaining Work
 % Complete

OK County Adult Detention Center - Baseline Schedule

TASK filters: Not Completed, Not

OK County Adult Detention Center - Baseline Schedule

17-Apr-26 Page 16 of 19 Pages

ActivityID	ActivityName	Orig Dur	Start	Finish	Percent Complete																																						
						2026												2027												2028												2029	
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
A22730	Earthwork - Building Pad - Area L	5	07-May-26	14-May-26	0%	Earthwork - Building Pad - Area L																																					
A1490	Drill Piers - Area L	10	10-Jun-26	24-Jun-26	0%	Drill Piers - Area L																																					
A1900	Form and Pour Grade Beams - Area L	10	24-Jun-26	09-Jul-26	0%	Form and Pour Grade Beams - Area L																																					
A21550	Coordination of Underground MEP - Area L	30	01-Jul-26	12-Aug-26	0%	Coordination of Underground MEP - Area L																																					
A2070	Concrete Curing - Area L	7	09-Jul-26	20-Jul-26	0%	Concrete Curing - Area L																																					
A16360	Install Underground MEP - Area L	15	13-Aug-26	02-Sep-26	0%	Install Underground MEP - Area L																																					
A1990	Pour SOG - Area L - P1	12	03-Sep-26	21-Sep-26	0%	Pour SOG - Area L - P1																																					
A2110	Pour SOG - Area L - P2	10	22-Sep-26	05-Oct-26	0%	Pour SOG - Area L - P2																																					
A2120	Excavate Retaining Walls - Loading Dock - Area L	8	06-Oct-26	15-Oct-26	0%	Excavate Retaining Walls - Loading Dock - Area L																																					
A21820	Pour SOG - Area L - P3	10	06-Oct-26	19-Oct-26	0%	Pour SOG - Area L - P3																																					
A2130	Form & Pour Retaining Walls - Loading Dock - Area L	10	16-Oct-26	29-Oct-26	0%	Form & Pour Retaining Walls - Loading Dock - Area L																																					
A2140	Grade and Form Loading Dock Ramps - Area L	8	30-Oct-26	10-Nov-26	0%	Grade and Form Loading Dock Ramps - Area L																																					
A2150	Form and Pour Loading Dock Ramps - Area L	5	11-Nov-26	17-Nov-26	0%	Form and Pour Loading Dock Ramps - Area L																																					
A21630	Overhead Coordination - Area L	34	23-Dec-26	10-Feb-27	0%	Overhead Coordination - Area L																																					
A19430	Erect Precast Walls - Area L - South Half	10	13-Jan-27	26-Jan-27	0%	Erect Precast Walls - Area L - South Half																																					
A19440	Erect Precast Walls - Area L - North Half	10	27-Jan-27	09-Feb-27	0%	Erect Precast Walls - Area L - North Half																																					
A16670	Install HSS Columns - Area L	10	10-Feb-27	23-Feb-27	0%	Install HSS Columns - Area L																																					
A16640	Install Roof Joists - Area L	10	24-Feb-27	09-Mar-27	0%	Install Roof Joists - Area L																																					
A16650	Lay Roof Decking - Area L	10	10-Mar-27	23-Mar-27	0%	Lay Roof Decking - Area L																																					
A18640	Set Roof Units - Area L	5	24-Mar-27	30-Mar-27	0%	Set Roof Units - Area L																																					
A21700	Install SOG Leave Outs - Area L	10	24-Mar-27	06-Apr-27	0%	Install SOG Leave Outs - Area L																																					
A18530	Install Roofing - Area L	12	31-Mar-27	15-Apr-27	0%	Install Roofing - Area L																																					
A16660	Remove Precast Bracing - Area L	5	07-Apr-27	13-Apr-27	0%	Remove Precast Bracing - Area L																																					
A17030	OH Plumbing Rough In - Storm - Area L	8	07-Apr-27	16-Apr-27	0%	OH Plumbing Rough In - Storm - Area L																																					
A17050	Set HM/Detention Frames in CMU - Area L	15	14-Apr-27	04-May-27	0%	Set HM/Detention Frames in CMU - Area L																																					
A17460	Build CMU Walls - Area L	20	14-Apr-27	11-May-27	0%	Build CMU Walls - Area L																																					
A18550	Install Overhead Doors - Area L	5	16-Apr-27	22-Apr-27	0%	Install Overhead Doors - Area L																																					
A18540	Install Exterior Doors and Louvers - Area L	10	16-Apr-27	29-Apr-27	0%	Install Exterior Doors and Louvers - Area L																																					
A18600	Install Exterior Windows - Area L	10	16-Apr-27	29-Apr-27	0%	Install Exterior Windows - Area L																																					
A17060	OH Plumbing Rough In - Domestic - Area L	20	19-Apr-27	14-May-27	0%	OH Plumbing Rough In - Domestic - Area L																																					
A17080	OH Hydronic Rough In - Area L	25	19-Apr-27	21-May-27	0%	OH Hydronic Rough In - Area L																																					
A22110	Substantially Dry - Area L	0		29-Apr-27	0%	Substantially Dry - Area L																																					
A18560	Place Elastomeric Coating - Area L	15	30-Apr-27	20-May-27	0%	Place Elastomeric Coating - Area L																																					
A17420	In-Wall Fire Suppression Rough In - Area L	5	12-May-27	18-May-27	0%	In-Wall Fire Suppression Rough In - Area L																																					
A17040	Electrical Room Build Out - Area L	10	12-May-27	25-May-27	0%	Electrical Room Build Out - Area L																																					
A17020	In-Wall Electrical Rough In - Area L	15	12-May-27	02-Jun-27	0%	In-Wall Electrical Rough In - Area L																																					
A19320	Install Exterior Lighting - Area L	10	21-May-27	04-Jun-27	0%	Install Exterior Lighting - Area L																																					
A17090	Duct Overhead Rough In - Area L	20	24-May-27	21-Jun-27	0%	Duct Overhead Rough In - Area L																																					
A17070	OH Electrical Rough In - Area L	20	26-May-27	23-Jun-27	0%	OH Electrical Rough In - Area L																																					
A22920	Install Drywall - Area L	5	03-Jun-27	09-Jun-27	0%	Install Drywall - Area L																																					
A19330	Install Exterior Security - Area L	15	07-Jun-27	25-Jun-27	0%	Install Exterior Security - Area L																																					
A22930	Tape/Float/Coat Walls - Area L	5	10-Jun-27	16-Jun-27	0%	Tape/Float/Coat Walls - Area L																																					
A18570	Set AHU - Area L	5	22-Jun-27	28-Jun-27	0%	Set AHU - Area L																																					
A17100	OH Fire Suppression Rough In - Area L	15	22-Jun-27	13-Jul-27	0%	OH Fire Suppression Rough In - Area L																																					
A17470	Insulate Overhead Lines - Area L	20	22-Jun-27	20-Jul-27	0%	Insulate Overhead Lines - Area L																																					

Start Date: 12-Jan-26

Data Date: 17-Apr-26

Run Date: 21-Apr-26



Remaining Level of Effort



Actual Level of Effort



Actual Work



Rem Work



Near Crit Rem



Remaining Work



Near Critical Remaining



Critical Remaining Work



% Complete

OK County Adult Detention Center - Baseline
Schedule

[illegible]

Start Date: 12-Jan-26

Data Date: 17-Apr-26

Run Date: 21-Apr-26

 Remaining Level of Effort

 Actual Level of Effort

Actual Level C

Actual Work

 Rem Work

 Near Crit Rem

 Near Crit Path
 Remaining Work

 Near Critical Remaining

 Critical Remaining Work

 Critical Return

 % Complete

OK County Adult Detention Center - Baseline Schedule

TASK filters: Not Completed, Not

OK County Adult Detention Center - Baseline Schedule

17-Apr-26 Page 18 of 19 Pages

ActivityID	ActivityName	Orig Dur	Start	Finish	Percent Complete	2026												2027												2028												2029		
						pr	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	A	Sen	Oct	N	Dec	Jan	F	M			
A20630	Erect Steel - Mezz Deck - Area G	10	24-Mar-27	06-Apr-27	0%																																							
A20970	Lay & Detail Mezz Deck - Area G	5	07-Apr-27	13-Apr-27	0%																																							
A21680	Pour SOMD - Mezz -Area G	5	14-Apr-27	20-Apr-27	0%																																							
A21670	Set Mezz MEP Equipment - Area G	5	21-Apr-27	27-Apr-27	0%																																							
A20640	Install Roof Joists - Area G	15	28-Apr-27	18-May-27	0%																																							
A20650	Lay Roof Decking - Area G	10	19-May-27	02-Jun-27	0%																																							
A21690	Install SOG Leave Outs - Area G	10	03-Jun-27	16-Jun-27	0%																																							
A20530	Install Roofing - Area G	15	03-Jun-27	23-Jun-27	0%																																							
A20670	Remove Precast Bracing - Area G	5	17-Jun-27	23-Jun-27	0%																																							
A20680	OH Plumbing Rough In - Storm -Area G	10	17-Jun-27	30-Jun-27	0%																																							
A20540	Install Exterior Doors and Louvers - Area G	10	24-Jun-27	08-Jul-27	0%																																							
A20550	Install Exterior Windows - Area G	10	24-Jun-27	08-Jul-27	0%																																							
A20660	Build CMU Walls -Area G	20	24-Jun-27	22-Jul-27	0%																																							
A20690	OH Plumbing Rough In - Domestic -Area G	20	01-Jul-27	29-Jul-27	0%																																							
A20700	OH Hydronic Rough In - Area G	25	01-Jul-27	05-Aug-27	0%																																							
A22120	Substantially Dry - Area G	0		08-Jul-27	0%																																							
A20560	Place Elastomeric Coating - Area G	15	09-Jul-27	29-Jul-27	0%																																							
A20730	Electrical Room Build Out - Area G	10	23-Jul-27	05-Aug-27	0%																																							
A20720	In-Wall Electrical Rough In - Area G	15	23-Jul-27	12-Aug-27	0%																																							
A20770	Set HM/Detention Frames in CMU - Area G	15	23-Jul-27	12-Aug-27	0%																																							
A20800	Hang HM Doors and Hardware - Area G	15	23-Jul-27	12-Aug-27	0%																																							
A20570	Install Exterior Lighting - Area G	10	30-Jul-27	12-Aug-27	0%																																							
A20710	Duct Overhead Rough In - Area G	20	06-Aug-27	02-Sep-27	0%																																							
A20760	OH Electrical Rough In - Area G	20	06-Aug-27	02-Sep-27	0%																																							
A20580	Install Exterior Security - Area G	15	13-Aug-27	02-Sep-27	0%																																							
A20820	Install Access Control Devices - As Needed - Area G	15	13-Aug-27	02-Sep-27	0%																																							
A20780	Pull Branch Wire - Area G	5	03-Sep-27	10-Sep-27	0%																																							
A21880	Set AHU - Area G	5	03-Sep-27	10-Sep-27	0%																																							
A20740	OH Fire Suppression Rough In - Area G	15	03-Sep-27	24-Sep-27	0%																																							
A20750	Insulate Overhead Lines - Area G	20	03-Sep-27	01-Oct-27	0%																																							
A20790	Pull Fire Alarm Cable - Area G	10	13-Sep-27	24-Sep-27	0%																																							
A22660	Terminate Equipment at Wiring - Area G	10	13-Sep-27	24-Sep-27	0%																																							
A21940	Equipment Start Up - AHU G-1.01	5	27-Sep-27	01-Oct-27	0%																																							
A22650	In-Wall Fire Suppression Rough In - Area G	15	27-Sep-27	15-Oct-27	0%																																							
A21510	Circulate & Flush Hydronic Lines - Area G	15	04-Oct-27	22-Oct-27	0%																																							
A22670	Establish Conditioned Air - Area G	5	25-Oct-27	29-Oct-27	0%																																							
A24330	Conditioned Air Established - Area G	0		29-Oct-27	0%																																							
A20810	Fill and Paint CMU Walls - Area G	20	01-Nov-27	30-Nov-27	0%																																							
A20830	Frame Security Ceiling - Area G	15	01-Dec-27	21-Dec-27	0%																																							
A20840	Set Lights in Grid Ceiling - Area G	10	22-Dec-27	06-Jan-28	0%																																							
A20850	Set Fire Suppression in Ceiling -Area G	8	07-Jan-28	18-Jan-28	0%																																							
A22460	Install Flooring - Area G	10	07-Jan-28	20-Jan-28	0%																																							
A20860	Drop Ceiling Tile - Area G	8	19-Jan-28	28-Jan-28	0%																																							
A20870	Install Plumbing Fixtures - Area G	10	31-Jan-28	11-Feb-28	0%																																							
A20880	Install Millwork - Area G	10	31-Jan-28	11-Feb-28	0%																																							

Start Date: 12-Jan-26

Data Date: 17-Apr-26

Run Date: 21-Apr-26



Remaining Level of Effort



Actual Level of Effort



Actual Work



Rem Work



Near Crit Rem



Remaining Work



Near Critical Remaining



Critical Remaining Work



% Complete

OK County Adult Detention Center - Baseline
Schedule

ActivityID	Activity Name	Orig Dur	Start	Finish	Percent Complete																																									
						2026												2027												2028												2029				
						or	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	Aug	Sep	Oct	N	Dec	Jan	Feb	M	Apr	M	Jun	Jul	A	Sep	Oct	N	Dec	Jan	F	M					
A20890	Install Kitchen Equipment - Area G	10	31-Jan-28	11-Feb-28	0%																																									
A20900	Hook Up Kitchen Equipment - Area G	15	14-Feb-28	03-Mar-28	0%																																									
A20920	Install Misc Finishes - Area G	10	06-Mar-28	17-Mar-28	0%																																									
A22910	Fire Suppression Trimout - Area G	5	20-Mar-28	24-Mar-28	0%																																									
A20910	Electrical Trimout - Area G	10	20-Mar-28	31-Mar-28	0%																																									
A22710	Plumbing Trimout - Area G	10	20-Mar-28	31-Mar-28	0%																																									
A20930	Final Paint - Area G	10	03-Apr-28	14-Apr-28	0%																																									
A22010	Final Clean - Area G	5	17-Apr-28	21-Apr-28	0%																																									
A22020	Flintco Punch - Area G	5	24-Apr-28	28-Apr-28	0%																																									

OK County Adult Detention Center - Baseline
Schedule
