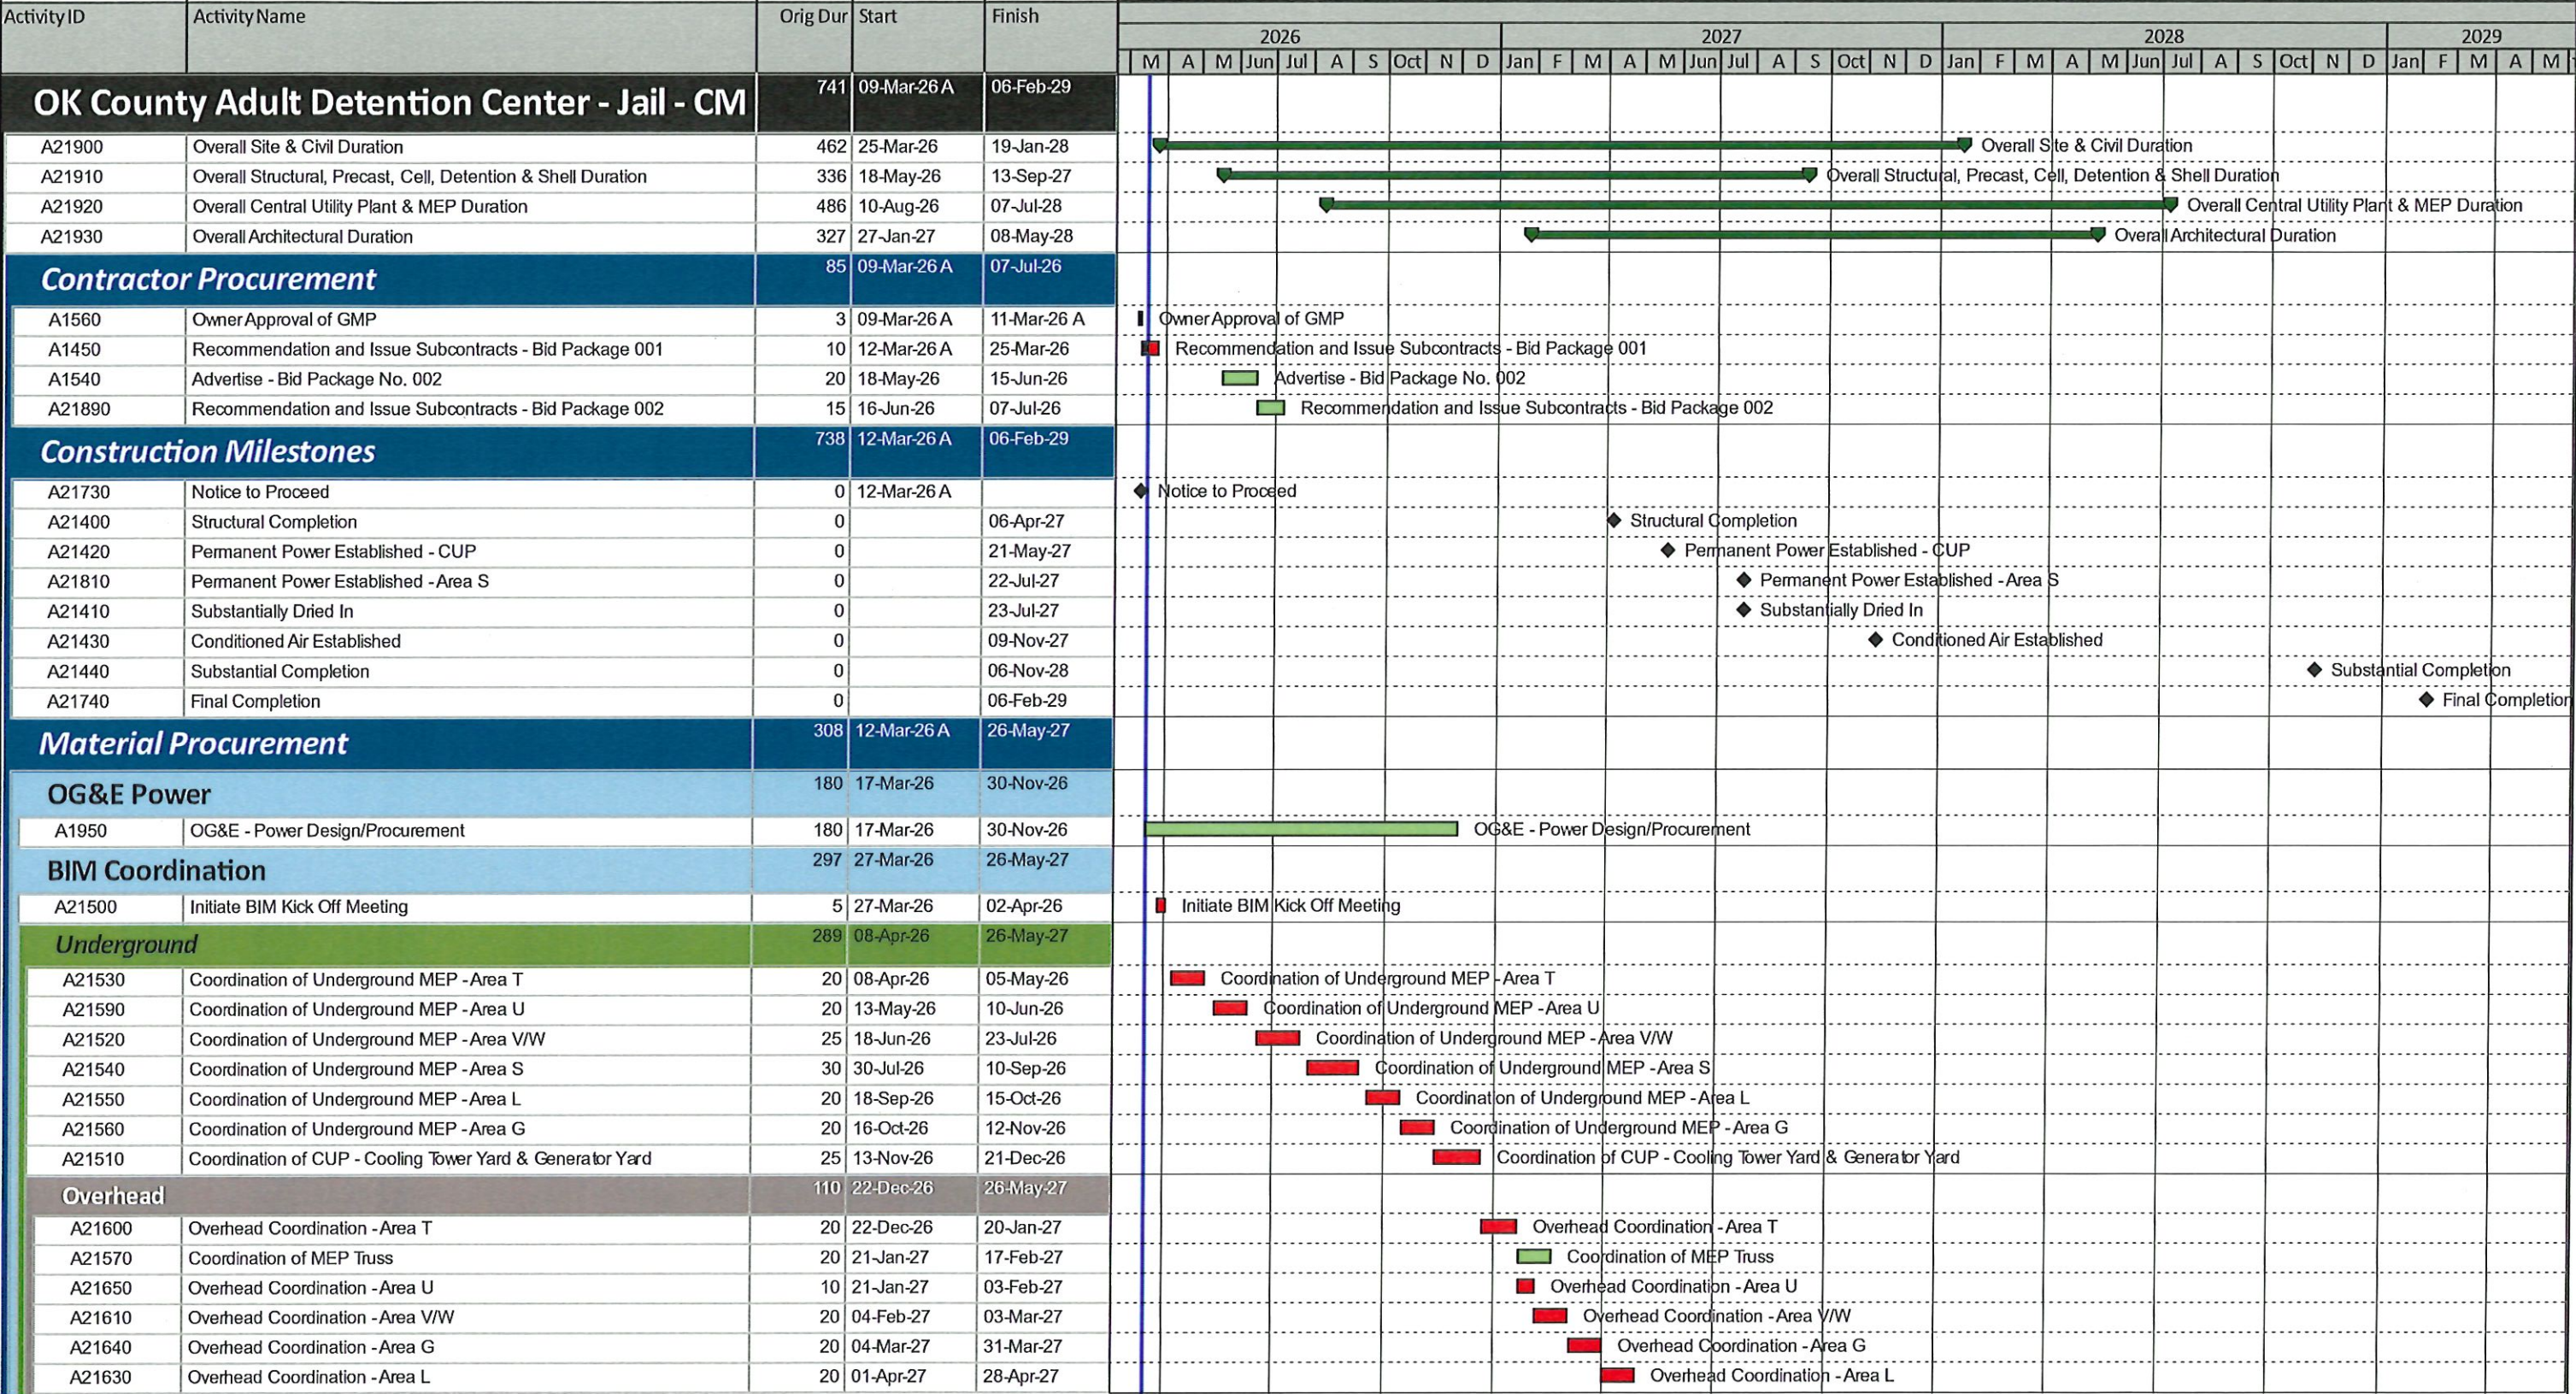


ActivityID	ActivityName	Orig Dur	Start	Finish	2026																2027												2028												2029				
					M	A	M	Jun	Jul	A	S	Oct	N	D	Jan	F	M	A	M	Jun	Jul	A	S	Oct	N	D	Jan	F	M	A	M	Jun	Jul	A	S	Oct	N	D	Jan	F	M	A	M						
A1970	Pour SOG -Area U - Pour 1	10	14-Aug-26	27-Aug-26																																													
Area V/W		75	24-Jul-26	06-Nov-26																																													
A1890	Form and Pour Grade Beams -Area V/W	10	24-Jul-26	06-Aug-26																																													
A16350	Install Underground MEP -Area V/W	30	07-Aug-26	18-Sep-26																																													
A16400	Excavate Pit -Area V	5	07-Aug-26	13-Aug-26																																													
A16410	Form and Pour Stem Walls -Pit -Area V	5	14-Aug-26	20-Aug-26																																													
A16420	Pour SOG - Pit -Area V	5	21-Aug-26	27-Aug-26																																													
A1980	Pour SOG -Area V/W - P1	5	21-Sep-26	25-Sep-26																																													
A2080	Form and Pour Platform	5	28-Sep-26	02-Oct-26																																													
A2040	Pour SOG -Area V/W - P2	10	05-Oct-26	16-Oct-26																																													
A2050	Pour SOG -Area V/W - P3	10	19-Oct-26	30-Oct-26																																													
A2060	Pour SOG -Area V/W - P4	5	02-Nov-26	06-Nov-26																																													
Area S		90	14-Aug-26	22-Dec-26																																													
A1910	Form and Pour Grade Beams -Area S	10	14-Aug-26	27-Aug-26																																													
A2010	Install Underground MEP -Area S	25	11-Sep-26	15-Oct-26																																													
A1940	Pour SOG -Area S - P1	10	09-Nov-26	20-Nov-26																																													
A2090	Pour SOG -Area S - P2	10	23-Nov-26	08-Dec-26																																													
A2100	Pour SOG -Area S - P3	10	09-Dec-26	22-Dec																																													

[illegible]

[illegible]

[illegible]

[illegible]

